
title: Build Work Estimate — Kestrel Financial Group -- Advisor Intelligence Platform (phases 1-2) author: Dewain Robinson build_platform: claude-code target_platform: both estimate_id: est_20260903T000000_kestrelcc generated: 2026-09-03T00:00:00Z

Build Work Estimate — Kestrel Financial Group

-- Advisor Intelligence Platform (phases 1-2)

Author: Dewain Robinson · **Estimate id:** est_20260903T000000_kestrelcc · **Generated:** 2026-09-03T00:00:00Z

SAMPLE — BUILD ESTIMATE ONLY, NOT A QUOTE

This document is generated by a **sample estimator** published as a demonstration of *how* an organization could build one. It is not a quote, a bid, a budget authority, or a commitment of any kind.

It estimates the work of building only — never the cost of running what gets built. Runtime, end-user licences, infrastructure, and human labour are all outside its scope and are not represented in any figure below.

The figures are estimates and will be wrong. They are derived from historical consumption patterns that may not resemble the work being estimated. Observed cost for comparable work in the calibration data spans more than 100x between the cheapest and most expensive instances. Treat the range as the estimate; treat the point figure as the midpoint of a guess.

Before any real budgeting use, this estimator must be modified for your organization — recalibrated against your own usage history, repriced against your contracted rates rather than list price, and adjusted for your own delivery patterns, model choices, and review overhead.

Rates verified 2026-09-03 and change without notice. Calibration source: measured · Generated 2026-09-03T00:00:00Z

Estimate summary

What was estimated

INPUT	VALUE
Built with (development tool)	Claude Code — metered in USD (tokens)
Built on (target environment)	Copilot Studio and Azure — metered in Copilot Credits + Azure consumption
Target harness	github-copilot — bills for build, test and evaluation
Licensing	Seat — Claude for Enterprise, \$150.00/month x 6 seats x 5 months = \$4,500.00 over the build
Specification	approved — confidence in sizing: high
Evaluation cycles planned	6
Contingency reserve	30%
Calibration	Measured, 24 local sessions

Totals

	BUILD — USD	TARGET — COPILOT CREDITS	COMBINED (USD)
Low	\$6,509.34	416,820	\$26,777.54
Likely	\$19,524.04	480,024	\$40,424.28
High	\$111,462.62	606,432	\$133,626.94
Likely + 30% reserve	\$25,381.25	624,031	\$52,551.56

Plan for \$40,424.28. Hold \$52,551.56 including the 30% reserve.

Two meters, not two options. The build and target figures are spent on the same project over the same period and add together; they are not alternatives to choose between.

- Copilot Credits are converted at \$0.01 each so the two meters can be shown in one column. They are separate budgets drawn on different accounts.
- The build figure is **notional** — on seat licensing no additional money is invoiced. See Licensing below for the share of the seat this build actually consumes.

- The build range comes from observed spread in comparable work; the target range from running 5 to 8 evaluation cycles instead of 6.

Everything below explains how each of these figures was reached.

What this was sized from

	REFERENCE
Functional specification	specification.md sections 1-4 (product and functional scope)
Technical specification	specification.md sections 5-9 (integration, Azure, data, NFRs, compliance)
Status	approved — Signed off. Sizes rest on agreed scope.
Confidence in sizing	high

Platforms

	PLATFORM	METERED IN
Built with	Claude Code	USD (tokens)
Built on	Copilot Studio and Azure	Copilot Credits + Azure consumption

These are different questions and different meters, and the same project spends on **both**. The building happens in a coding agent authoring the agent definition; the target platform is where it is deployed, previewed, evaluated and validated. Copilot Studio is a destination, not a build tool.


This is not a platform comparison tool. It reports one chosen build platform and one chosen target, each in its own meter. Platform decisions are not made on cost alone — capability, existing skills, governance, integration, and support all matter more than a build-time figure — and using this report to pick a platform would be using it for something it was not designed to answer.

Scope — this estimates the build, not the run

This figure covers the work of **building** the thing. It does not cover operating it afterwards.

OUT OF SCOPE	WHERE TO GO INSTEAD
Runtime / operational cost of what gets built	Copilot Studio agent usage estimator
End-user seat licences (M365 Copilot, Power Platform)	Your licensing/procurement process
Infrastructure, hosting, storage, egress	Your cloud cost tooling
Human labour — PM, design, QA time	Your delivery estimation process
Ongoing maintenance and support after delivery	A run cost, not a build cost

The build loop

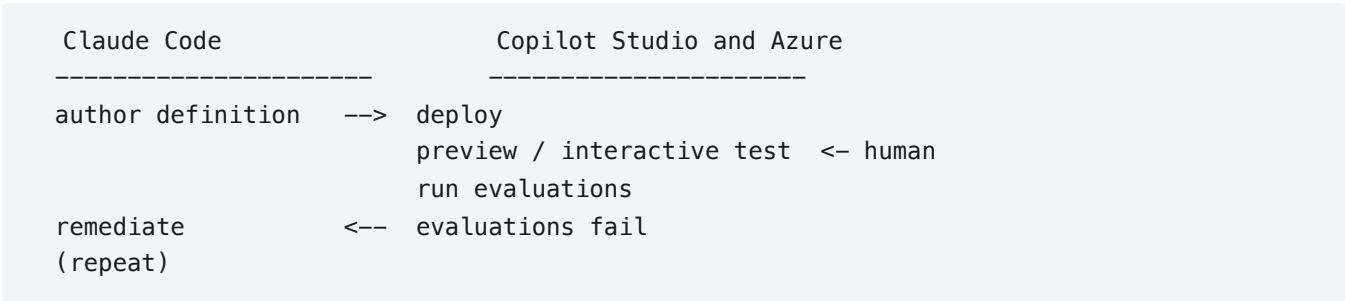

This estimate plans **6 evaluation cycles**. Each cycle after the first adds **25%** of the original build back as remediation, giving a build-side multiplier of **2.25x**. An estimate that prices only the first pass is planning for a build where every evaluation passes first time.

Build — Claude Code

	AMOUNT
Base estimate (incl. remediation)	\$19,524.04
Reserve (30%)	\$5,857.21
Budget ask	\$25,381.25
Observed low	\$6,509.34
Observed high	\$111,462.62

Reserve adequacy

The reserve does not cover observed variance.

A **30%** reserve reaches \$25,381.25. Comparable work has reached \$111,462.62. Full coverage would require **471%**.

ITEM	SIZE	FILES	TURNS	ESTIMATE	RANGE	N
Custodial core contract and rate-limit discovery	exploration (brownfield)	0	128	\$47.20	\$10.35 – \$2,210.15	7
Entitlement model mapping to book-of-business	exploration (brownfield)	0	128	\$47.20	\$10.35 – \$2,486.43	7
Agent foundation - instructions, orchestration, memory scoping	medium	8	1,044	\$384.30	\$84.67 – \$1,963.82	5
C1 Client position summary	large	6	1,980	\$728.64	\$303.59 – \$4,044.74	3
C2 Transaction enquiry	medium	4	1,044	\$384.30	\$84.67 – \$1,636.52	5
C3 Review pack assembly	large	9	1,980	\$728.64	\$303.59 – \$4,622.56	3
C4 Document retrieval and request	medium	5	1,044	\$384.30	\$84.67 – \$1,636.52	5
C5 Suitability record surfacing	medium	5	1,044	\$384.30	\$84.67 – \$2,291.11	5
C6 Disclosure orchestration	large	10	1,980	\$728.64	\$303.59 – \$4,622.56	3
C7 Service request triage	medium	6	1,044	\$384.30	\$84.67 – \$1,963.82	5
C8 Complaint detection and escalation	large	7	1,980	\$728.64	\$303.59 – \$4,622.56	3
C9 Market and product context	small	4	371	\$136.62	\$74.52 – \$536.72	6
Tool schemas, auth paths and error handling (18 tools)	large	20	1,980	\$728.64	\$303.59 – \$4,044.74	3
Write-path confirmation, idempotency and audit (7 write tools)	large	12	1,980	\$728.64	\$303.59 – \$4,622.56	3
Knowledge indexing pipeline and effective dating	medium	8	1,044	\$384.30	\$84.67 – \$2,291.11	5
Console shell, Entra ID auth, routing and role gating	medium	9	1,044	\$384.30	\$84.67 – \$1,636.52	5

ITEM	SIZE	FILES	TURNS	ESTIMATE	RANGE	N
Agent conversation surface with citation rendering	large	10	1,980	\$728.64	\$303.59 – \$4,044.74	3
Position and performance visualisation	large	11	1,980	\$728.64	\$303.59 – \$3,466.91	3
Review pack builder and preview	large	14	1,980	\$728.64	\$303.59 – \$4,622.56	3
Disclosure tracker and suitability panel	medium	9	1,044	\$384.30	\$84.67 – \$1,963.82	5
Service request queue and document library	medium	11	1,044	\$384.30	\$84.67 – \$1,636.52	5
Audit viewer, WCAG 2.2 AA conformance, telemetry	medium	12	1,044	\$384.30	\$84.67 – \$1,963.82	5
Client self-service portal (auth, accounts, documents, messaging)	large	16	1,980	\$728.64	\$303.59 – \$4,044.74	3
Session and token brokering, agent invocation relay	large	9	1,980	\$728.64	\$303.59 – \$4,044.74	3
Aggregation endpoints for position and review views	medium	7	1,044	\$384.30	\$84.67 – \$1,963.82	5
Write-path confirmation orchestration	large	8	1,980	\$728.64	\$303.59 – \$4,622.56	3
Rate limiting, quota and circuit breaking	small	5	371	\$136.62	\$74.52 – \$536.72	6
Custodial core integration (positions, transactions, batch)	large (brownfield)	14	2,970	\$1,092.96	\$455.40 – \$6,067.10	3
Dynamics 365 integration	medium (brownfield)	8	1,566	\$576.45	\$127.01 – \$2,945.72	5
Document management and e-signature integration	medium (brownfield)	9	1,566	\$576.45	\$127.01 – \$2,945.72	5
Market data and KYC screening integration	medium (brownfield)	8	1,566	\$576.45	\$127.01 – \$3,436.67	5
Supervision archive and notification fan-out	medium	8	1,044	\$384.30	\$84.67 – \$1,963.82	5

ITEM	SIZE	FILES	TURNS	ESTIMATE	RANGE	N
Disclosure rules service	large	10	1,980	\$728.64	\$303.59 – \$4,622.56	3
Landing zone extension, networking and private endpoints	medium (brownfield)	12	1,566	\$576.45	\$127.01 – \$2,945.72	5
API Management policies and gateway configuration	medium	9	1,044	\$384.30	\$84.67 – \$1,963.82	5
Cosmos data model, TTL and retention policies	medium	8	1,044	\$384.30	\$84.67 – \$1,963.82	5
AI Search indexes and semantic configuration	medium	7	1,044	\$384.30	\$84.67 – \$1,963.82	5
Observability, alerting and dashboards	small	8	371	\$136.62	\$74.52 – \$536.72	6
CI/CD and ALM for the agent definition and application	medium	11	1,044	\$384.30	\$84.67 – \$1,963.82	5

Calibration basis

Measured from 24 local sessions spanning 2026-06-01 to 2026-08-30.

Cost per agent turn: **\$0.32**, at **list price** — an organization on contracted rates must substitute its own.

Licensing

Seat-based licensing (Claude for Enterprise). Usage draws on an allowance already paid for, so no additional money changes hands for this build -- but the seat is not free.

Developer-months of allowance available	30 (6 seats x 5 months)
Share of that allowance	137%
Seat spend over the build	\$4,500.00
Attributable cost of this build	\$6,187.20
Already committed to other work	30%
Total committed	167%

The attributable cost is the seat's monthly price apportioned by the share of the allowance this build consumes. Nothing extra is invoiced, but this is the real cost of the capacity the build uses up.

Allowance overrun

This build plus existing workload exceeds the allowance by 67%.

Work will stall at the limit unless overage is enabled, at which point it bills on top of the seat. Overage exposure at the same rate: \$3,037.20.

Options: spread the build across allowance periods, move part of it to consumption billing, add seats, or reduce the other committed work.

Window risk

Seat allowances refill on 5-hour rolling and weekly windows, not only monthly. A build that fits comfortably in a month can still exhaust a short window and stall.

Notional value at list rates: \$19,524.04 — what this build would cost on consumption billing. Shown for scale; it is not a charge.

Target platform — Microsoft Copilot Studio

Target harness: github-copilot — GitHub Copilot harness bills from the moment you start building. Creating a solution with natural language, previewing, testing, and generating evaluations all consume credits. Credits cover LLM tokens, tools (knowledge and MCPs), and the harness itself.

BUILD-AND-TEST ACTIVITY	CREDITS	AT \$0.01/CC	BASIS
Interactive validation in the Copilot Studio interface	100,800	\$1,008.00	96.0 human hours x 25 interactions/hour = 2,400 interactions
Evaluation runs	378,288	\$3,782.88	568 cases x 3 repeats x 6 cycles = 10,224 runs
Agent flow runs during build and test	936	\$9.36	7,200 actions across 6 cycles at 13 CC per 100 -- test runs in the designer and test chat are exempt
Total	480,024	\$4,800.24	
Reserve (30%)	144,007	\$1,440.07	required contingency
Budget ask	624,031	\$6,240.31	

Reasoning-model surcharge: 385,764 credits (\$3,857.64). Reasoning models bill the feature rate plus the premium token tier, so the effective tier is premium whatever the standard tier selected.

The evaluation loop

Evaluation is not a one-off gate. Microsoft's guidance is an explicit cycle — define tests, run evaluations, analyse results, improve the agent, repeat — with a target pass rate of 80–90% and near 100% on core tests.

This estimate plans **6 cycles**: 10,224 evaluation runs in total, plus the remediation each failed cycle sends back to the build platform.

Velocity, not just cost. Evaluations are capped at **20 per agent node per day**, so this volume needs a minimum of **516 days** of elapsed time however much budget is available.

Human validation — a dependency, not a cost line

96.0 hours of interactive validation are planned in the Copilot Studio interface. Those hours are collected to size the test volume above — they are **not** estimated as labour cost, consistent with this tool metering agent consumption rather than people.

Someone must go into the interface, confirm behaviour, and make configuration changes between cycles. That step gates the loop, and no amount of build budget removes it.

Not included

- Production runtime once the agent is live
- Agent flow test runs in the designer or test chat (documented exemption)
- Capacity pack sizing and overage enforcement
- End-user Microsoft 365 Copilot licence offsets
- Human hours for validation (collected to size test volume only)

For production runtime consumption use Microsoft's [agent usage estimator](#).

Rates verified 2026-09-03. Sources: [billing rates](#) · [harness billing](#) · [evaluation limits](#) · [iteration guidance](#)

Target platform — Azure

Azure consumption during build and test, as supplied. Azure rates are not bundled here — they depend entirely on the services chosen.

ITEM	USD
App Service and Functions (dev/test/staging)	\$2,400.00
Cosmos DB (three environments)	\$3,100.00
Azure AI Search with semantic ranking	\$4,200.00
API Management	\$2,800.00
Service Bus, Storage, Key Vault	\$900.00
Observability ingestion	\$1,600.00
Front Door and networking	\$1,100.00
Reserve (30%)	\$4,830.00
Budget ask	\$20,930.00

Known limits

1. **Build only.** Nothing here is the cost of running the agent once it is live.
2. **Human validation is a dependency, not a line item.** Hours are collected to size test volume, never estimated as labour.
3. **Turn counts are the weakest input,** and thin buckets are flagged above.
4. **Rates go stale.** Re-verify against the sources cited.
5. **This is a sample.** Modify it for your organization before budgeting use.

Close the loop

```
python record_actual.py est_20260903T000000_kestrelcc --sessions <session-id> [...]
```

SAMPLE — build estimate only, not a quote. Excludes runtime cost. Modify for your organization before budgeting use.
